


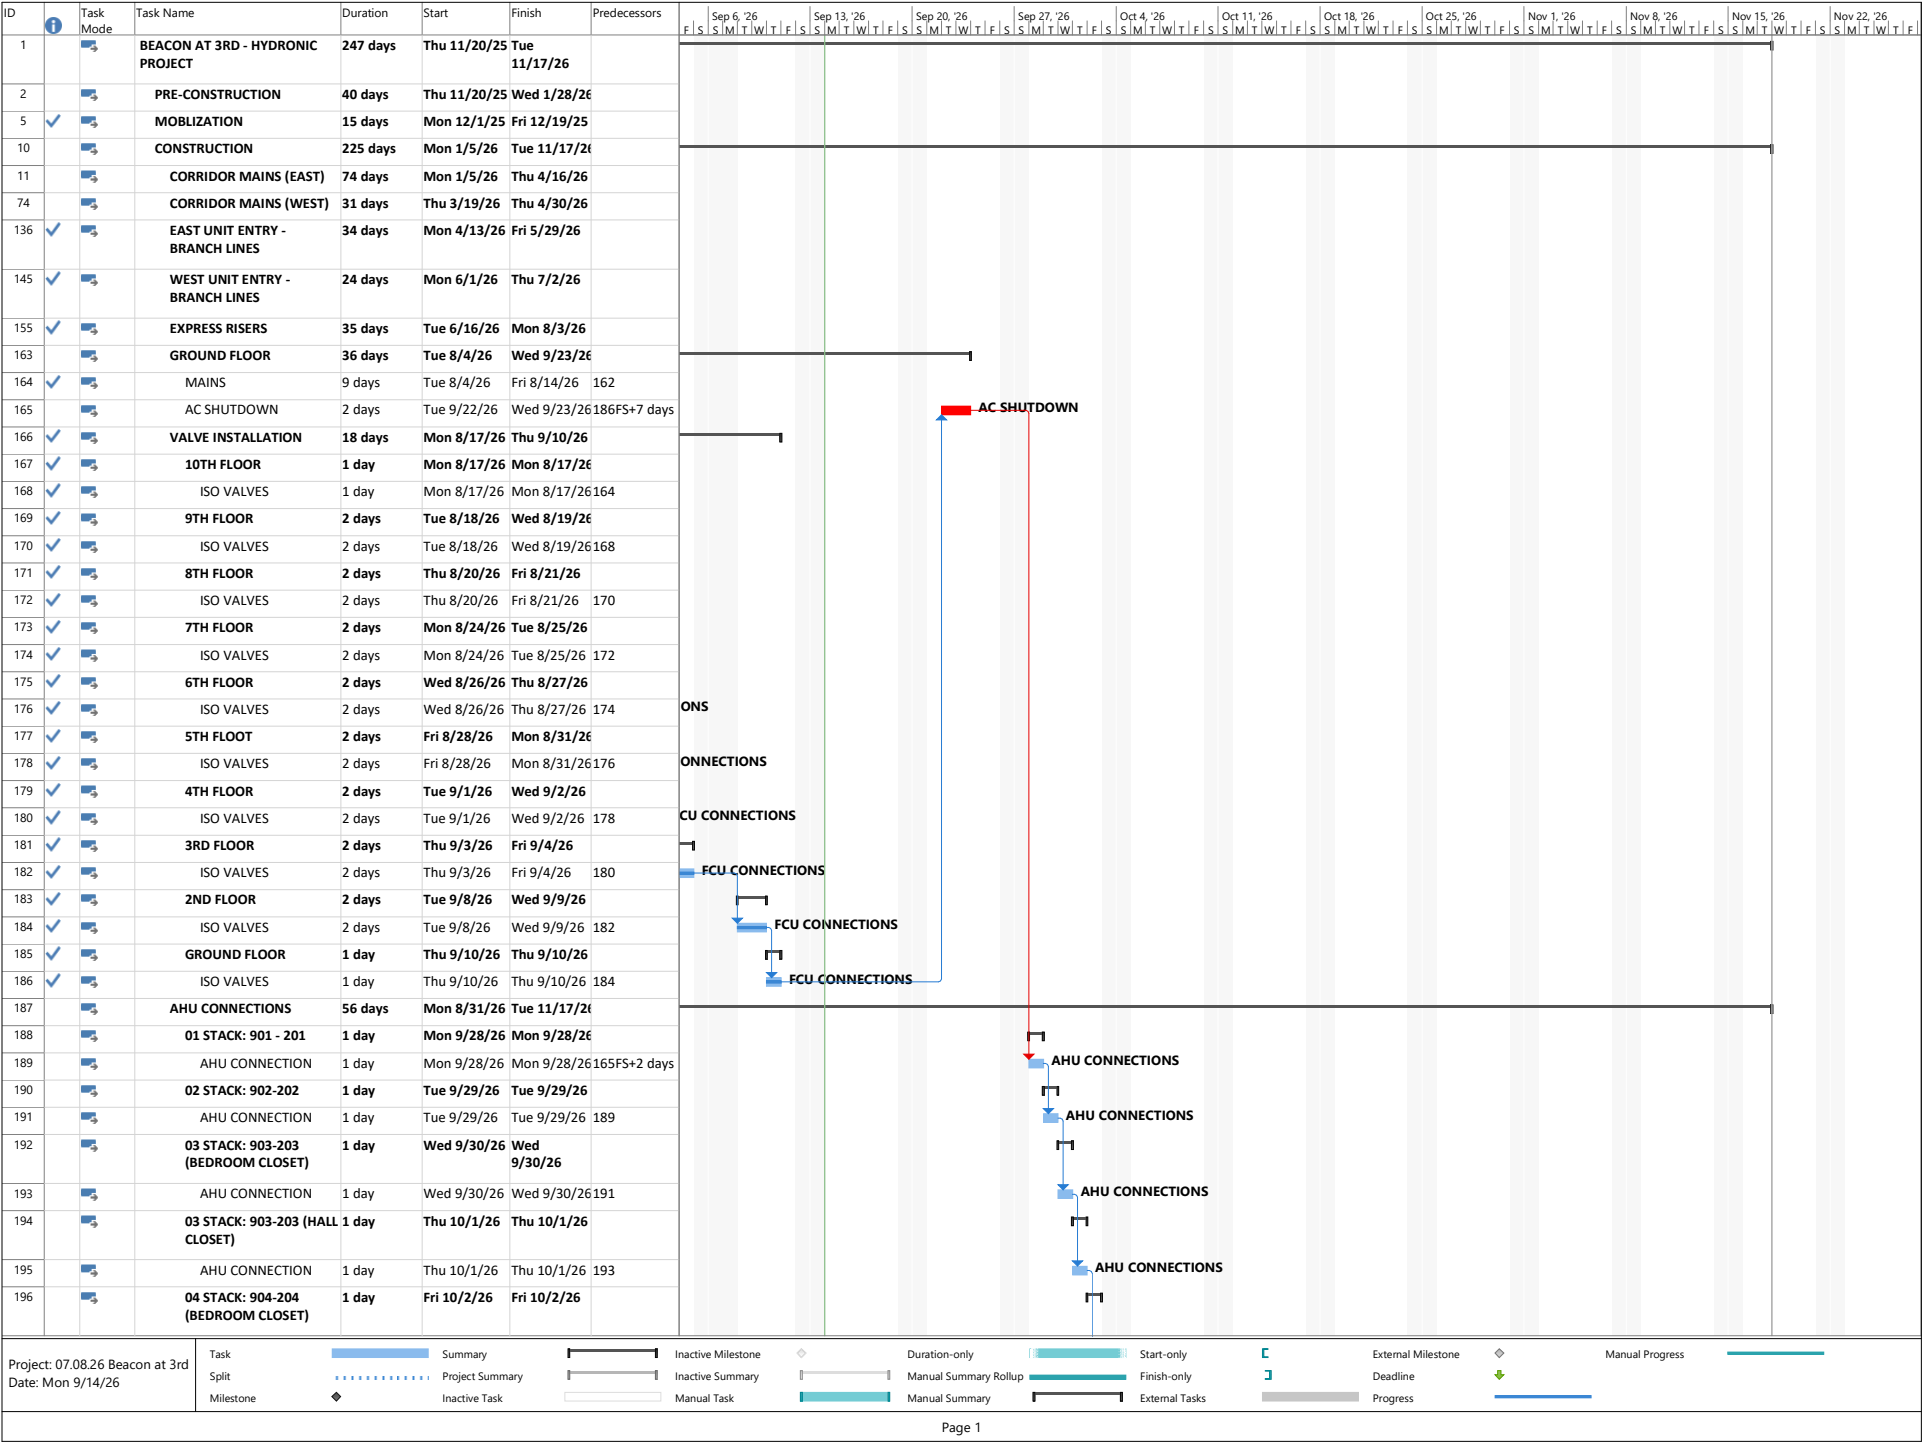

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Sep 6, '26	Sep 13, '26	Sep 20, '26	Sep 27, '26	Oct 4, '26	Oct 11, '26	Oct 18, '26	Oct 25, '26	Nov 1, '26	Nov 8, '26	Nov 15, '26	Nov 22, '26
197		AHU CONNECTION	1 day	Fri 10/2/26	Fri 10/2/26	195												
198		04 STACK: 904-204 (HALL CLOSET)	1 day	Mon 10/5/26	Mon 10/5/26													
199		AHU CONNECTION	1 day	Mon 10/5/26	Mon 10/5/26	197												
200		05 STACK: 905-205	1 day	Tue 10/6/26	Tue 10/6/26													
201		AHU CONNECTION	1 day	Tue 10/6/26	Tue 10/6/26	199												
202		06 STACK: 906-206	1 day	Wed 10/7/26	Wed 10/7/26													
203		AHU CONNECTION	1 day	Wed 10/7/26	Wed 10/7/26	201												
204		07 STACK: 907-207 (BEDROOM CLOSET)	1 day	Thu 10/8/26	Thu 10/8/26													
205		AHU CONNECTION	1 day	Thu 10/8/26	Thu 10/8/26	203												
206		07 STACK: 907-207 (HALLWAY CLOSET)	1 day	Fri 10/9/26	Fri 10/9/26													
207		AHU CONNECTION	1 day	Fri 10/9/26	Fri 10/9/26	205												
208		08 STACK: 908-208 (BEDROOM CLOSET)	1 day	Mon 10/12/26	Mon 10/12/26													
209		AHU CONNECTION	1 day	Mon 10/12/26	Mon 10/12/26	207												
210		08 STACK: 908-208 (HALL CLOSET)	1 day	Tue 10/13/26	Tue 10/13/26													
211		AHU CONNECTION	1 day	Tue 10/13/26	Tue 10/13/26	209												
212		11 STACK: 911-211 (BEDROOM CLOSET)	1 day	Wed 10/14/26	Wed 10/14/26													
213		AHU CONNECTION	1 day	Wed 10/14/26	Wed 10/14/26	211												
214		11 STACK: 911-211 (HALL CLOSET)	1 day	Thu 10/15/26	Thu 10/15/26													
215		AHU CONNECTION	1 day	Thu 10/15/26	Thu 10/15/26	213												
216		12 STACK: 912-212 (BEDROOM CLOSET)	1 day	Fri 10/16/26	Fri 10/16/26													
217		AHU CONNECTION	1 day	Fri 10/16/26	Fri 10/16/26	215												
218		12 STACK: 912-212 (HALL CLOSET)	1 day	Mon 10/19/26	Mon 10/19/26													
219		AHU CONNECTION	1 day	Mon 10/19/26	Mon 10/19/26	217												
220		15 STACK: 1015-215	1 day	Tue 10/20/26	Tue 10/20/26													
221		AHU CONNECTION	1 day	Tue 10/20/26	Tue 10/20/26	219												
222		16 STACK: 1016-216	1 day	Wed 10/21/26	Wed 10/21/26													
223		AHU CONNECTION	1 day	Wed 10/21/26	Wed 10/21/26	221												
224		17 STACK: 1017-217	1 day	Thu 10/22/26	Thu 10/22/26													
225		AHU CONNECTION	1 day	Thu 10/22/26	Thu 10/22/26	223												
226		18 STACK: 1018-218	1 day	Fri 10/23/26	Fri 10/23/26													
227		AHU CONNECTION	1 day	Fri 10/23/26	Fri 10/23/26	225												
228		09 STACK: 909-209 (BEDROOM CLOSET)	1 day	Mon 10/26/26	Mon 10/26/26													
229		AHU CONNECTION	1 day	Mon 10/26/26	Mon 10/26/26	227												
230		09 STACK: 909-209 (HALL CLOSET)	1 day	Tue 10/27/26	Tue 10/27/26													
231		AHU CONNECTION	1 day	Tue 10/27/26	Tue 10/27/26	229												
232		10 STACK: 910-210 (BEDROOM CLOSET)	1 day	Wed 10/28/26	Wed 10/28/26													
233		AHU CONNECTION	1 day	Wed 10/28/26	Wed 10/28/26	231												

Project: 07.08.26 Beacon at 3rd
Date: Mon 9/14/26

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Progress

Manual Progress

Page 2

